



CAPE HENLOPEN SCHOOL DISTRICT

SCHOOL CONSTRUCTION EXAMINATION
FISCAL YEAR ENDED JUNE 30, 2022



CAPE HENLOPEN SCHOOL DISTRICT

REPORT SUMMARY FISCAL YEAR ENDED JUNE 30, 2022

BACKGROUND

An examination engagement of the Cape Henlopen School District Schedule of Construction Projects to determine whether it is in accordance with the criteria set forth in the Delaware Code. The State of Delaware Department of Education School Construction Technical Assistance Manual, and the State of Delaware Budget and Accounting Policy Manual.

In accordance with 29 Del. C. §7526, the State Auditor is mandated to conduct post-audits of any school construction improvement authorized by a school construction bond authorization act. This engagement was performed to examine financial data, recordkeeping and reports generated by the school district and related to Bond Bill construction projects.

KEY INFORMATION AND FINDINGS

Since fiscal year 2017, state and local funding for Cape Henlopen School District totaled nearly \$223.3 million in construction appropriations, including \$27 million expended in FY2022. Our responsibility is to obtain reasonable assurance by evaluating the Schedule of Construction Projects against the criteria set forth in the Delaware Code, the State of Delaware Department of Education School Construction Technical Assistance Manual, and the State of Delaware Budget and Accounting Policy Manual and performing other procedures to obtain sufficient appropriate evidence to express an opinion that conveys the results of our evaluation.

We have examined the Cape Henlopen School District's financial data, recordkeeping and reports related to its Schedule of Construction Projects for the fiscal year ended June 30, 2022, to determine whether the district's Capital Budget process was in accordance with the criteria set forth in the Delaware Code, the State of Delaware Department of Education School Construction Technical Assistance Manual and the State of Delaware Budget and Accounting Policy Manual.

This engagement contained one finding on the Schedule of Construction Projects for Cape Henlopen School District as stated below:

- The Schedule of Construction Projects was not accurately presented in that it erroneously reported an increase in funding of \$450,000 for appropriation 50188 as original funding.

Note: Schedule on page 3 of the report reflects the corrected Expended n Prior Years amounts for this project.



CAPE HENLOPEN SCHOOL DISTRICT


REPORT SUMMARY FISCAL YEAR ENDED JUNE 30, 2022

KEY INFORMATION AND FINDINGS

Cape Henlopen School District Summary of Active Project Capital Funding

FY	Total Funding to Date	Total Expended to Date	Balance as of 6/30/22
2017	\$ 21,555,900	\$ 21,512,755	\$ -
2018	\$ 48,495,501	\$ 48,287,032	\$ 39,990
2019	\$ 44,215,529	\$ 43,029,384	\$ 454,092
2020	\$ 31,414,459	\$ 30,570,706	\$ 843,753
2021	\$ 60,898,800	\$ 44,490,908	\$ 16,407,892
2022	\$ 23,727,000	\$ -	\$ 23,727,000
Total:	\$ 230,307,189	\$ 188,834,462	\$ 41,472,727

Cape Henlopen
Total Funding and Remaining Project Balance by Fiscal Year

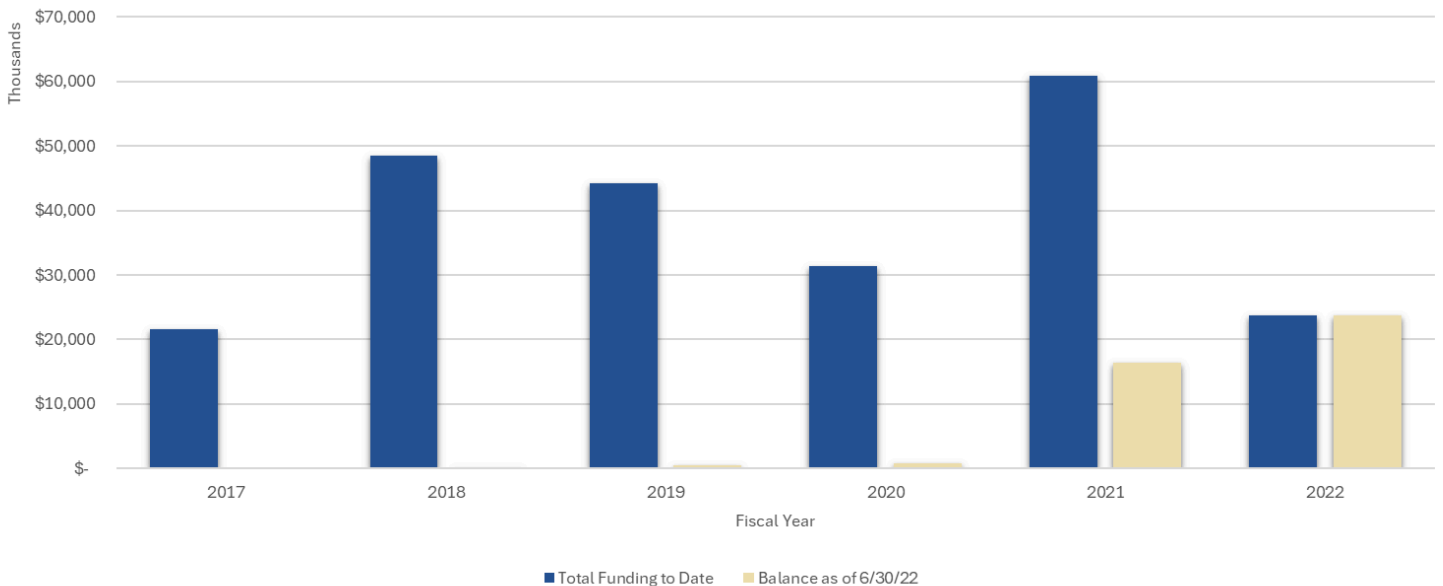

**CAPE HENLOPEN SCHOOL DISTRICT
STATEWIDE SCHOOL DISTRICT CONSTRUCTION
PROJECT EXAMINATION ENGAGEMENT
FISCAL YEAR ENDED JUNE 30, 2022**

BACKGROUND

School District Construction Projects

In accordance with 29 Del. C. §7509, the Department of Education (DOE) shall determine the present necessity for any school construction program. Once a School District (the District) identifies the need for a construction project and receives approval from its local Board of Education (the Board), it submits a request for Certificate of Necessity to the DOE by August 31 each year. The DOE then meets with the District to review appropriate documentation and discuss the necessity of the project. If it is deemed necessary, the DOE will include the project in its budget request for the following fiscal year. All projects that are included in the budget request are then issued a Certificate of Necessity (CN) by late October of each fiscal year, which authorizes the construction project and details the scope and cost limits for the project.¹

The DOE calculates the amount of the State of Delaware (the State) funding the District will receive using a standard school construction formula. The formula is uniform throughout the State and is based on pupil capacity for the type of school requested (i.e., elementary, middle, or high school). The remainder of the cost is paid with local tax receipts, thus referred to as the local share. Before a District can issue bonds to fund the local share of the construction costs, taxpayers must approve the bond sale through a referendum.² A referendum may occur any time after a CN is issued, and the District has one year and two opportunities to pass a successful referendum before needing to request a new CN from the DOE. The timing of each referendum is at the discretion of the Board. Vocational-Technical Districts are not subject to the referendum process. Instead, the Legislature approves these Districts' tax rates.³

The District must provide adequate public notice of the referendum that includes the purpose and amount of the proposed bond issuance, as well as the estimated annual amount of tax increase upon approval.⁴ The estimated increase, however, is based on certain assumptions that are subject to change, such as the anticipated interest rate on new bonds.⁵ Therefore, taxpayers are voting on the approval of the construction project and cannot rely on the advertised referendum rate as the effective tax rate. The District may ask its taxpayers to approve a local share in excess of the school construction formula to finance additional options. For example, if a construction project included expanding a particular school building and the District wished to continue the same flooring throughout the entire building, taxpayers may be asked to fund the costs in excess of the State formula. This particular request must be clearly labeled on the referendum voting ballot using the language set forth in 14 Del C. §2004.

¹ DOE's School Construction Technical Assistance Manual, Section 1.10, *Summary of Steps in the Major Capital Improvement Process*

² 14 Del. C. §2122

³ 14 Del. C., c. 26

⁴ 14 Del. C. §1074 (b)

⁵ Other rates that are not subject to voter approval (e.g., tuition, minor capital improvements) may be increased by the District to meet annual demands, thus resulting in the effective tax rate for the District.

The DOE presents its budget of all the State's Districts' construction projects to the Office of Management and Budget for approval and inclusion in the Governor's Recommended Budget. ⁶ The Governor's Recommended Budget is then subject to final approval by the Bond Bill Committee and the Legislature via the Bond and Capital Improvements Act (also referred to as the Bond Bill). If a District fails to obtain a successful referendum before June 30, its project is removed from the Governor's Recommended Budget and not included in that year's Bond Bill.

The District's Board then has the "power to employ engineers, architects and such other employees as it deems essential..." for its construction project per 29 Del. C. §7521. All final plans and specifications, including costs of construction under any school construction bond authorization act, are approved by the DOE. ⁷

Depending on various factors (e.g., the total cost of the project, other projects within the State), the District will receive funding for its construction project over the course of several fiscal years. For each State bond sale, the District receives an aggregate allocation of funds and must pay back a portion of those funds with local tax receipts. The local share for each District in the State can vary,⁸ depending on an assessment of the District's ability to meet its obligations. ⁹

The District coordinates with the Office of the State Treasurer to pay the local share of its outstanding principal and interest payments in accordance with 14 Del. C. §2108. Annually, the Office of Auditor of Accounts audits the Districts' local tax collections and debt service management in a separate engagement. Further, this engagement examines Bond Bill construction project expenditures.

In the event the construction project comes in under budget, the District may request permission from the State legislature to redirect the State-funded portion of the excess budget amount to fund another project. The subsequent epilogue language in the Bond Bill dictates if the District must put forth local tax receipts and what sources of funding the District may use, such as Minor Capital Improvement funds. Since this is a result of Delaware law, the change does not require a referendum.

There are no legal or statutory provisions that would prohibit a District from utilizing excess funds for early repayment of its debt.

Maintenance of Records

The District should maintain all appropriate documentation related to its construction projects and related debt, including documents related to the referendum process, for audit purposes.

⁶ Same as footnote 1

⁷ 29 Del. C. §7518

⁸ 29 Del. C. §7503 (b)

⁹ An Equalization Committee, as defined by 14 Del. C. §1707 (j), is comprised of 10 to 15 members appointed by the Secretary of the DOE. The equalization formula (detailed in 14 Del. C. §1707) incorporates an annual survey conducted by the University of Delaware and is annually reviewed and approved by the Equalization Committee.

TABLE OF CONTENTS

	<u>PAGE</u>
INDEPENDENT ACCOUNTANT'S REPORT	1
SCHEDULE OF CONSTRUCTION PROJECTS	3
SCHEDULE OF CURRENT YEAR FINDINGS	4



INDEPENDENT ACCOUNTANT'S REPORT

Mr. Robert Fulton
Superintendent
Cape Henlopen School District
1270 Kings Highway
Lewes, Delaware 19958

The Honorable Mark A. Holodick, Ed.D.
Secretary, Department of Education
Townsend Building, Suite 2
401 Federal Street
Dover, Delaware 19901

We have examined the accompanying State of Delaware Cape Henlopen School District (the District) Schedule of Construction Projects for the fiscal year ended June 30, 2022 to determine whether it is in accordance with the criteria set forth in the Delaware Code, the State of Delaware Department of Education School Construction Technical Assistance Manual (SCM), and the State of Delaware Budget and Accounting Policy Manual (BAM). The District's management is responsible for the presentation of the Schedule of Construction Projects in accordance with the criteria set forth in the Delaware Code, the SCM, and the BAM. Our responsibility is to obtain reasonable assurance by evaluating the Schedule of Construction Projects against the criteria set forth in the Delaware Code, the SCM, and the BAM and performing other procedures to obtain sufficient appropriate evidence to express an opinion that conveys the results of our evaluation based on our examination.

Our examination was conducted in accordance with the attestation standards for a direct examination engagement established by the American Institute of Certified Public Accountants and the standards applicable to attestation engagements contained in *Government Auditing Standards* issued by the Comptroller General of the United States. Those standards require that we obtain reasonable assurance by evaluating the District's presentation of the Schedule of Construction Projects for the fiscal year ended June 30, 2022 against the criteria set forth in the Delaware Code, the SCM, and the BAM and performing other procedures to obtain sufficient appropriate evidence to express an opinion that conveys the results of our evaluation of the District's presentation of the Schedule of Construction Projects for the fiscal year ended June 30, 2022. The nature, timing, and extent of the procedures selected depend on our judgment, including an assessment of the risks that the District's Schedule of Construction Projects was not in accordance with the criteria set forth in the Delaware Code, the SCM, and the BAM in all material respects, whether due to fraud or error. We believe that the evidence we obtained is sufficient and appropriate to provide a reasonable basis for our opinion.

We are required to be independent of the District, and to meet our other ethical responsibilities, in accordance with relevant ethical requirements relating to our examination engagement.

In our opinion, the District's Schedule of Construction Projects for the fiscal year ended June 30, 2022 presents fairly, in all material respects, based on the criteria set forth in the Delaware Code, the SCM, and the BAM.

Mr. Robert Fulton
Cape Henlopen School District

The Honorable Mark A. Holodick, Ed.D.
Department of Education

The amounts reported in the Expended in Prior Years column of the Schedule of Construction Projects contain expenditures incurred prior to July 1, 2019 that were examined by other accountants. The fiscal year ended June 30, 2019 report dated March 3, 2021, expressed an unmodified opinion on the Schedule of Construction Projects. As a result, we did not examine expenditures incurred prior to July 1, 2019 reported in the Expended in Prior Years column of the Schedule of Construction Projects for the fiscal year ended June 30, 2022 and, therefore, express no opinion on it.

In accordance with *Government Auditing Standards*, we are required to report all deficiencies that are considered to be significant deficiencies or material weaknesses in internal control; fraud and noncompliance with provisions of laws or regulations that have a material effect on the District's Schedule of Construction Projects; and any other instances that warrant the attention of those charged with governance, noncompliance with provisions of contracts or grant agreements, and abuse that has a material effect on the subject matter. We are also required to obtain and report the views of responsible officials concerning the findings, conclusions, and recommendations, as well as any planned corrective actions. We performed our examination to express an opinion on whether District's Schedule of Construction Projects is presented in accordance with the criteria described above and not for the purpose of expressing an opinion on the internal control applicable to preparing the District's Schedule of Construction Projects or on compliance and other matters; accordingly, we express no such opinion. Our examination disclosed a certain finding that is required to be reported under *Government Auditing Standards* and this finding, along with the views of responsible officials, are described in the attached Schedule of Current Year Findings.

This report is intended solely for the information and use of District management and board members, the Office of Auditor of Accounts, and the Department of Education and is not intended to be, and should not be, used by anyone other than these specified parties. However, under 29 Del. C. §10002, this report is public record, and its distribution is not limited. This report, as required by statute, was provided to the Office of the Governor, Office of the Controller General, General Assembly, Office of the Attorney General, and Office of Management and Budget.

Barbacane, Thornton & Company LLP
BARBACANE, THORNTON & COMPANY LLP

Wilmington, Delaware
April 18, 2024

**SCHEDULE OF CONSTRUCTION PROJECTS
FISCAL YEAR ENDED JUNE 30, 2022**

Project Name	FY	APPR	Source of Funding (State/Local)	Original Funding Amount	Increases (Decreases) in Funding	Market Pressure Funding	Total Funding to Date	Expended in Prior Years	Expended in Current Year	Total Expended to Date	Balance as of 6/30/2022
Cape Henlopen High School	2019	50188	100/0	\$ -	\$ 450,000	\$ -	\$ 450,000	\$ 443,892	\$ -	\$ 443,892	\$ 6,108
Milton Elementary School	2019	50467	60/40	8,968,900	(100,000)	-	8,868,900	8,567,326	260,500	8,827,826	41,074
Milton Elementary School	2020	50467	60/40	2,989,667	-	2,969,645	5,959,312	5,801,718	109,580	5,911,298	48,014
Milton Elementary School	2021	50467	60/40	17,937,800	-	-	17,937,800	12,839,610	4,642,517	17,482,127	455,673
Rehoboth Elementary School	2018	50474	60/40	12,655,700	-	-	12,655,700	12,652,639	-	12,652,639	3,061
Rehoboth Elementary School	2019	50474	60/40	12,655,500	-	-	12,655,500	12,655,500	-	12,655,500	-
Rehoboth Elementary School	2020	50474	60/40	-	3,396,500	-	3,396,500	3,326,827	67,739	3,394,566	1,934
Rehoboth Elementary School	2021	50474	60/40	3,646,500	(3,646,500)	-	-	-	-	-	-
Rehoboth Elementary School/SC	2018	50476	100/0	2,346,500	-	-	2,346,500	2,346,500	-	2,346,500	-
Rehoboth Elementary School/SC	2019	50476	100/0	2,346,500	(110,000)	-	2,236,500	2,236,500	-	2,236,500	-
Richard Shields Elementary	2019	50482	60/40	10,325,600	(7,000,000)	-	3,325,600	3,023,313	111,113	3,134,426	191,174
Richard Shields Elementary	2020	50482	60/40	3,441,833	2,153,500	3,059,962	8,655,295	7,586,731	843,890	8,430,621	224,674
Richard Shields Elementary	2021	50482	60/40	20,651,200	3,646,500	-	24,297,700	4,676,749	15,650,594	20,327,343	3,970,357
Sussex Consortium	2017	50490	100/0	6,733,200	535,000	-	7,268,200	7,243,604	24,596	7,268,200	-
Sussex Consortium	2018	50490	100/0	13,466,300	-	-	13,466,300	13,325,733	105,485	13,431,218	35,082
Sussex Consortium	2019	50490	100/0	2,244,400	110,000	-	2,354,400	2,304,171	13,562	2,317,733	36,667
HOB Elementary School	2017	50491	60/40	12,053,000	-	-	12,053,000	12,046,451	6,549	12,053,000	-
HOB Elementary School	2018	50491	60/40	12,052,900	-	-	12,052,900	12,015,426	37,474	12,052,900	-
HOB Elementary School	2021	50491	60/40	3,646,500	(450,000)	-	3,196,500	555,050	2,119,965	2,675,015	521,485
Cape Henlopen High School	2019	50492	60/40	4,172,500	-	-	4,172,500	3,814,289	205,354	4,019,643	152,857
Cape Henlopen High School	2020	50492	60/40	8,345,000	-	-	8,345,000	7,913,911	381,820	8,295,731	49,269
Cape Henlopen High School	2021	50492	60/40	1,390,800	-	-	1,390,800	1,090,244	215,195	1,305,439	85,361
HOB Elementary School/SC	2017	50493	100/0	2,234,700	-	-	2,234,700	2,222,700	12,000	2,234,700	-
HOB Elementary School/SC	2018	50493	100/0	2,234,800	-	-	2,234,800	2,229,863	4,937	2,234,800	-
Cape Henlopen High School/SC	2019	50496	100/0	187,700	-	-	187,700	178,451	4,297	182,748	4,952
Cape Henlopen High School/SC	2021	50496	100/0	212,600	-	-	212,600	94,424	70,292	164,716	47,884
Sussex Consortium additional funds	2019	50497	100/0	2,964,429	7,000,000	-	9,964,429	9,805,942	137,227	9,943,169	21,260
Sussex Consortium additional funds	2020	50497	100/0	10,782,952	(7,000,000)	-	3,782,952	3,119,152	166,414	3,285,566	497,386
New Middle School	2021	50499	60/40	11,863,400	2,000,000	-	13,863,400	884,247	1,652,021	2,536,268	11,327,132
New Middle School	2022	50499	60/40	23,727,000	-	-	23,727,000	-	-	-	23,727,000
Sussex Consortium Supplemental	2018	59945	100/0	5,739,301	-	-	5,739,301	5,716,871	20,583	5,737,454	1,847
Cape Henlopen High School /SC	2020	59971	100/0	1,275,400	-	-	1,275,400	1,115,833	137,091	1,252,924	22,476
Construction Projects Total				\$ 223,292,582	\$ 985,000	\$ 6,029,607	\$ 230,307,189	\$ 161,833,667	\$ 27,000,795	\$ 188,834,462	\$ 41,472,727

**SCHEDULE OF CURRENT YEAR FINDINGS
JUNE 30, 2022**

Finding 2022-1

Criteria

Internal Control – Integrated Framework, published by the Committee of Sponsoring Organizations of the Treadway Commission, defines control activities as “policies and procedures that help ensure management directives are carried out.” Control activities occur throughout an organization, at all levels and functions, and include a wide range of activities, such as authorizations, verifications, reconciliations, reviews of operating performance, security of assets, and segregation of duties. To ensure control activities meet the objectives of management, supporting documentation for all such activities should be referred to or maintained with the financial documents. Management review controls are defined as activities of a person different than the preparer analyzing and performing oversight of activities performed and is an integral part of any internal control structure.

Management review of the Schedule of Construction Projects is required by Cape Henlopen School District internal controls.

Condition

We noted that the Schedule of Construction Projects prepared by the District did not properly present information, as detailed below:

- The funding source for each appropriation reported on the Schedule of Construction Projects was incorrect.
- The Schedule of Construction Projects erroneously reported increase in funding of \$450,000 for appropriation 501 88 (Cape Henlopen High School) as original funding.

Note: The Schedule of Construction Projects included on page 3 on this report reflects the corrected Expended in Prior Years amounts for this project.

Cause

Management of the District did not provide proper oversight regarding the review of amounts included in the Schedule of Construction Projects.

Effect

The Schedule of Construction Projects was not accurately presented.

Recommendation

We recommend that the District develop and implement a management review process to ensure accurate representation of the financial data within the Schedule of Construction Projects.

District's Response

The District agrees with the finding. This was as a result of a clerical error during the preparation of the Schedule of Construction Projects.
